





Project: WRS Move ver 2
Date: Thu 05/02/15



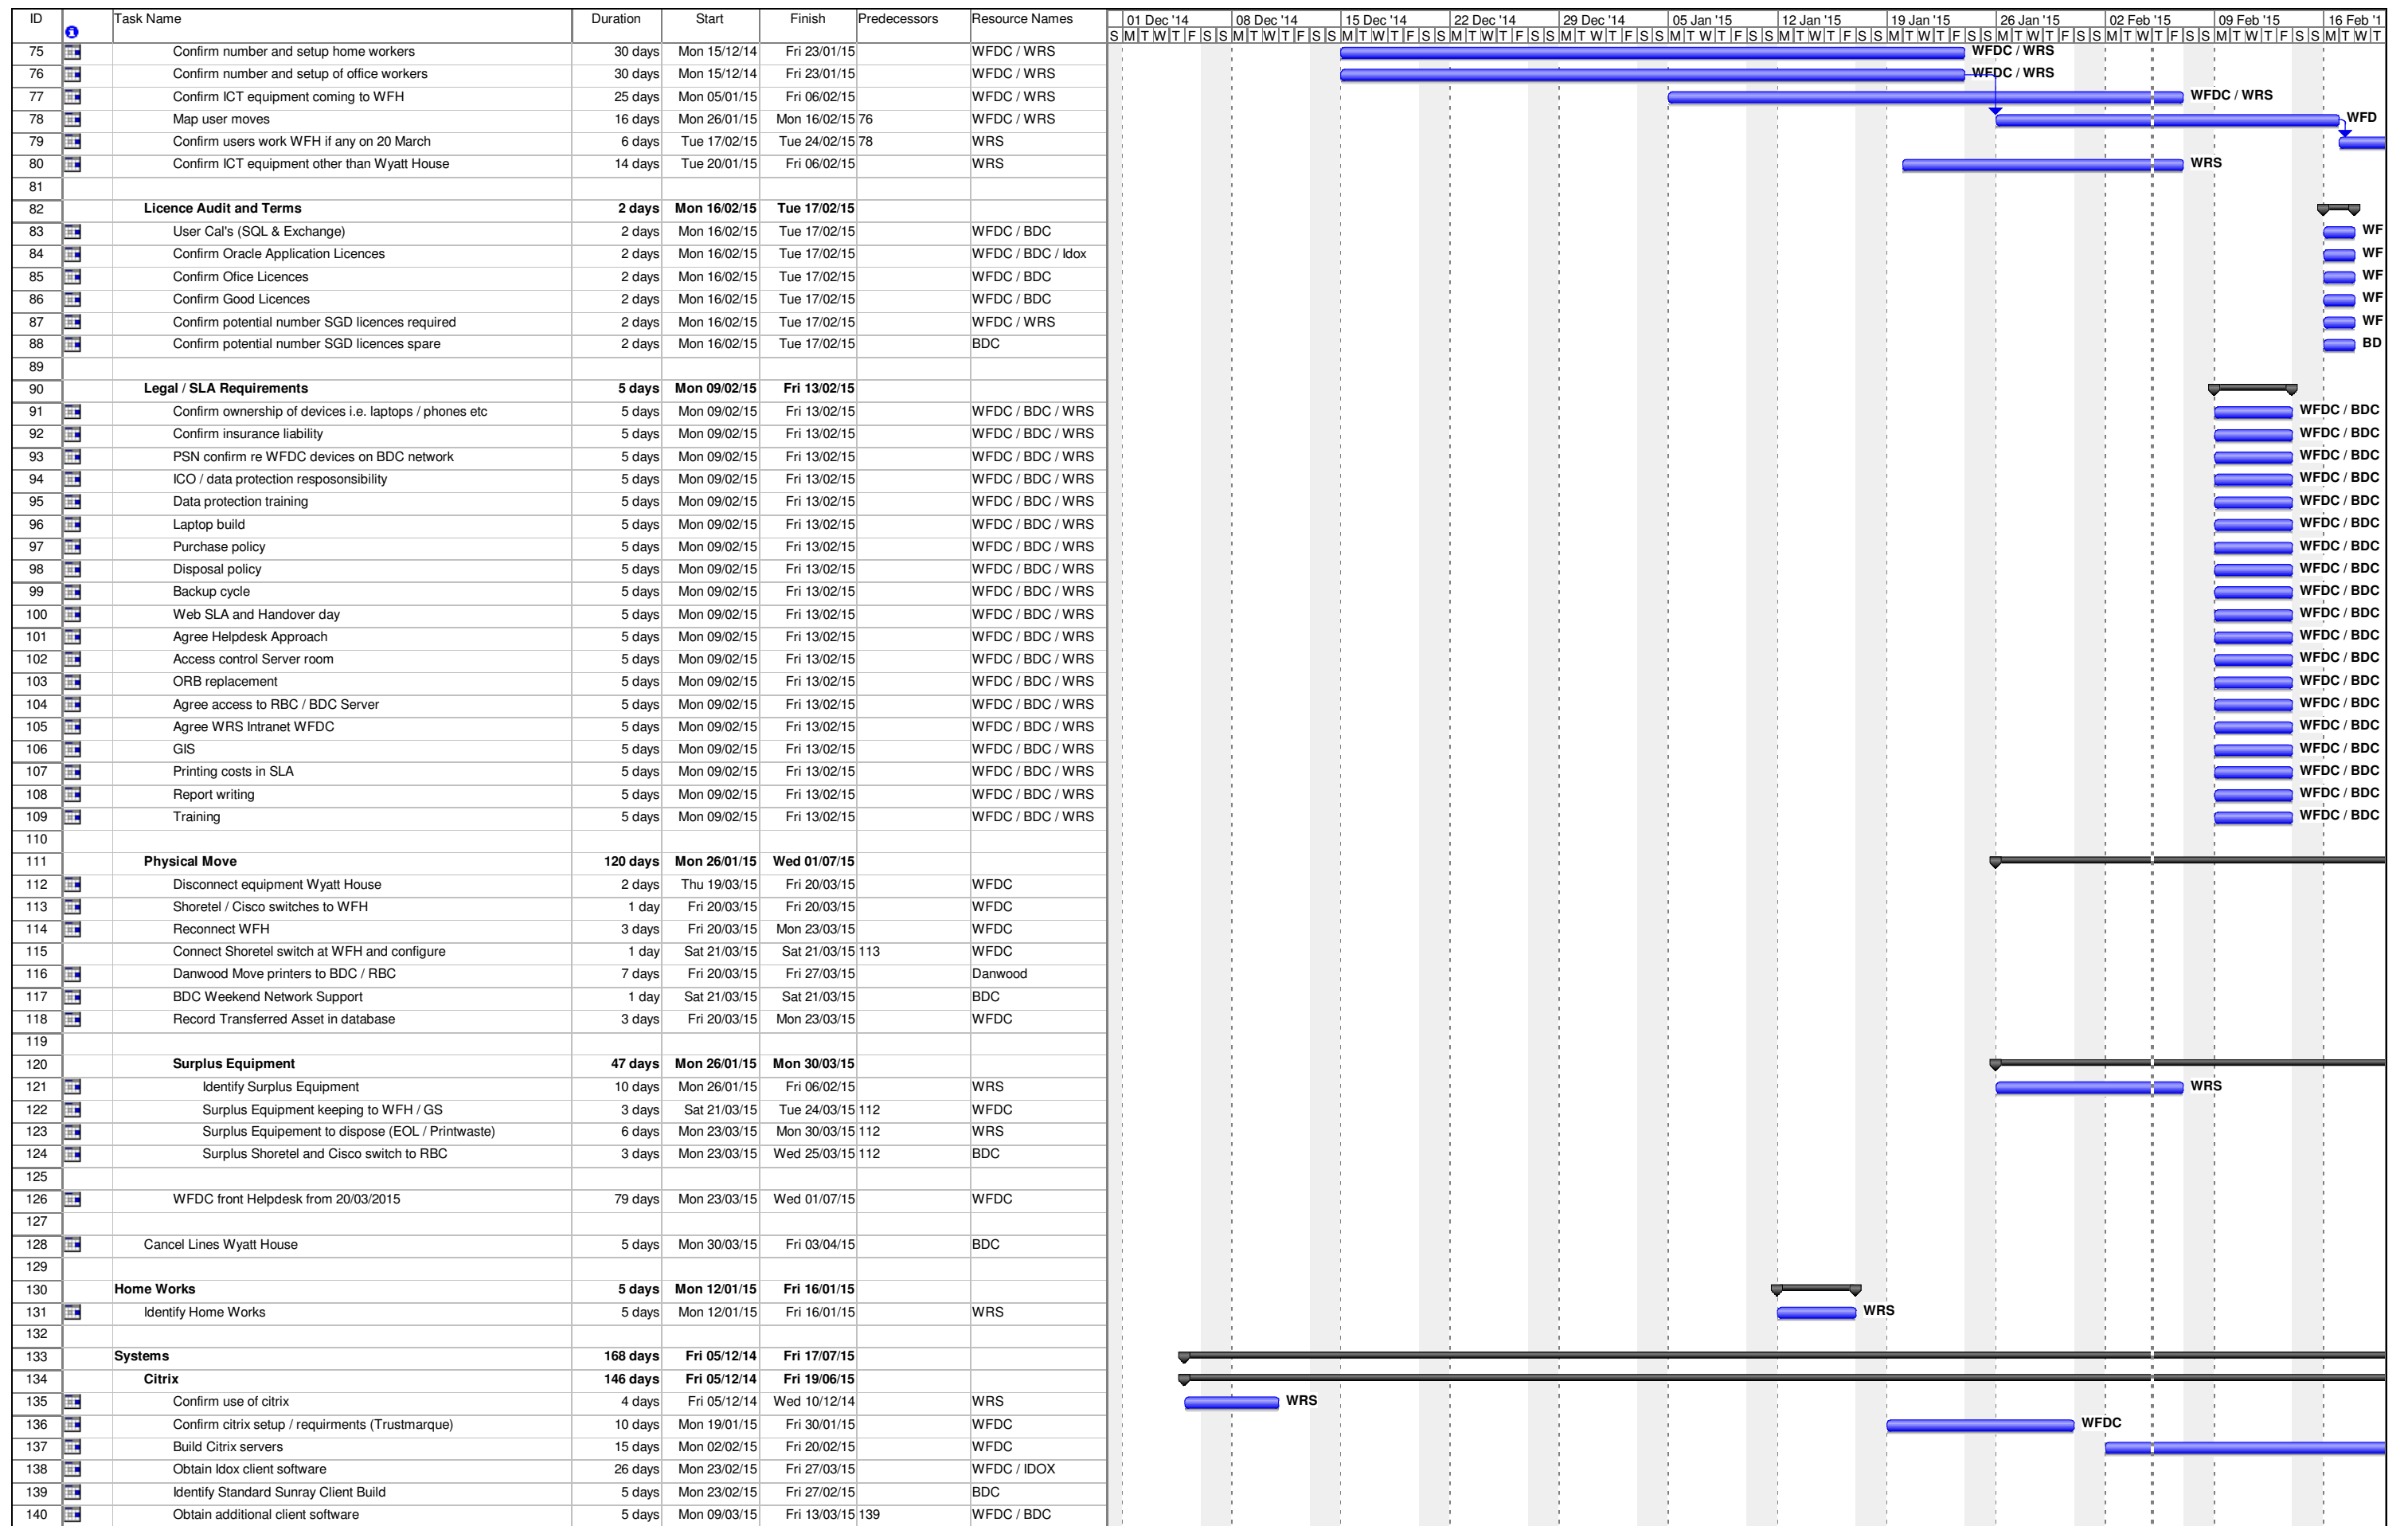

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	2014							2015								
							01 Dec '14	08 Dec '14	15 Dec '14	22 Dec '14	29 Dec '14	05 Jan '15	12 Jan '15	19 Jan '15	26 Jan '15	02 Feb '15	09 Feb '15	16 Feb '15				
207	WRS sign off live email migrations	4 days	Thu 18/06/15	Sun 21/06/15		WRS																
208	Good Setup / iPads	124 days	Thu 22/01/15	Fri 03/07/15																		
209	Obtain Tablet if possible and check setup / apps	2 days	Thu 22/01/15	Fri 23/01/15		WRS																
210	Agree approach WRS	1 day	Mon 23/02/15	Mon 23/02/15		WFDC / WRS																
211	Identify priority staff	1 day	Tue 24/02/15	Tue 24/02/15	210	WFDC / WRS																
212	Supply smart phones configured with Good	1 day	Mon 01/06/15	Mon 01/06/15		WFDC																
213	Wipe Ipads and reconfigure	10 days	Mon 22/06/15	Fri 03/07/15		WFDC / BDC																
214	Agree GCSX email approach initial meeting	1 day	Mon 01/06/15	Mon 01/06/15		WFDC / BDC																
215	Update / clear down BDC Exchange	5 days	Mon 13/07/15	Fri 17/07/15	204	BDC																
216																						
217	Active Directory	122 days	Mon 09/02/15	Fri 17/07/15																		
218	Create users and accounts	10 days	Mon 09/02/15	Fri 20/02/15		WFDC																
219	List of Requirements to BDC	2 days	Mon 23/02/15	Tue 24/02/15		WFDC																
220	Identify distribution Groups, Permissions etc and migration plan	2 days	Mon 02/03/15	Tue 03/03/15	219	WFDC / BDC / WRS																
221	Complete setup	24 days	Wed 04/03/15	Fri 03/04/15	220	WFDC																
222	Agree on-going reporting re changes	1 day	Fri 03/04/15	Fri 03/04/15		WFDC / BDC																
223	On-Going maintenance	28 days	Mon 04/05/15	Mon 08/06/15	222	WFDC																
224	Go-live WFDC Dom / Cease BDC	2 days	Sat 20/06/15	Sun 21/06/15		BDC																
225	WRS User login acceptance testing	4 days	Thu 18/06/15	Sun 21/06/15		WRS																
226	Update / clear down BDC AD	5 days	Mon 13/07/15	Fri 17/07/15		BDC																
227																						
228	GIS	103 days	Wed 04/02/15	Fri 19/06/15																		
229	Identify Map Storage	4 days	Mon 09/02/15	Thu 12/02/15		WFDC																
230	Complete Questionnaires	4 days	Mon 09/02/15	Thu 12/02/15		WFDC																
231	Return Questionnaires	1 day	Fri 13/02/15	Fri 13/02/15	230	WFDC																
232	Confirm Idox connection to Map Store	1 day	Mon 16/02/15	Mon 16/02/15	231	IDOX																
233	Check GIS setup with RBC and WRS	5 days	Mon 09/02/15	Fri 13/02/15		WFDC / BDC / WRS																
234	Confirm other overlay data requirements	5 days	Mon 09/02/15	Fri 13/02/15		WFDC / BDC / WRS																
235	Confirm completion of Historical Mapping	5 days	Mon 09/02/15	Fri 13/02/15		BDC																
236	Clarify OS Data	5 days	Mon 09/02/15	Fri 13/02/15		WFDC MT																
237	Obtain mapping data OS	5 days	Mon 02/03/15	Fri 06/03/15		WFDC MT																
238	Obtain additional overlay data	5 days	Mon 02/03/15	Fri 06/03/15		WFDC MT																
239	Confirm address data connector installed PW	1 day	Mon 16/02/15	Mon 16/02/15		WFDC																
240	Database cut from BDC Uniform DB for Test earliest	1 day	Mon 23/02/15	Mon 23/02/15		RBC																
241	Download own address base	5 days	Mon 09/02/15	Fri 13/02/15		WFDC MT																
242	Load own addresses test data	5 days	Mon 30/03/15	Fri 03/04/15		WFDC MT																
243	Load address base / OS for live system	5 days	Mon 15/06/15	Fri 19/06/15		WFDC MT																
244	Investigate Licence requirement	1 day	Wed 04/02/15	Wed 04/02/15		WFDC / BDC																
245	Esri licence cost	1 day	Wed 04/02/15	Wed 04/02/15		BDC																
246	Esri Licence tools costs	1 day	Wed 04/02/15	Wed 04/02/15		BDC																
247																						
248	Other Systems (none WFDC Hosted) agree dates	98 days	Mon 26/01/15	Fri 05/06/15																		
249	Identify other systems requiring access	6 days	Mon 26/01/15	Mon 02/02/15		WRS / BDC																
250	Check access from none RBC domain	91 days	Wed 04/02/15	Fri 05/06/15																		
251	ORB	91 days	Wed 04/02/15	Fri 05/06/15																		
252	Check WRS re requirements	3 days	Wed 04/02/15	Fri 06/02/15		WFDC / WRS																
253	Initial Meeting re setup / requirements	1 day	Mon 13/04/15	Mon 13/04/15		WFDC / BDC / WRS																
254	Build Site / Pages	21 days	Tue 14/04/15	Fri 08/05/15	253	WFDC																
255	Load Content	20 days	Mon 11/05/15	Fri 05/06/15		WRS																
256	Chris 21	41 days	Mon 16/02/15	Fri 10/04/15																		
257	WRS live Feb	1 day	Mon 16/02/15	Mon 16/02/15		BDC																
258	URL to system	1 day	Mon 06/04/15	Mon 06/04/15		BDC																
259	Test access	4 days	Tue 07/04/15	Fri 10/04/15	258	WRS																
260	Cedar	88 days	Mon 09/02/15	Fri 05/06/15																		
261	Confirm WRS staff accessing system	5 days	Mon 09/02/15	Fri 13/02/15		WRS																
262	Confirm Web client access	1 day	Mon 06/04/15	Mon 06/04/15		BDC																
263	Obtain link	1 day	Mon 01/06/15	Mon 01/06/15		BDC																
264	Test access	4 days	Tue 02/06/15	Fri 05/06/15	263	WRS																
265	Identify additional systems / databases	5 days	Mon 09/02/15	Fri 13/02/15																		
266	Confirm any other system access required	5 days	Mon 09/02/15	Fri 13/02/15		WRS																
267																						
268	Policies	47 days	Mon 09/02/15	Mon 13/04/15																		
269	Agree on-going policy arrangements and reporting	1 day	Mon 09/02/15	Mon 09/02/15		WRS																
270	On-going arrangements for policy changes etc	1 day	Mon 13/04/15	Mon 13/04/15		BDC / WFDC / WRS																
271																						
272	Hardware	54 days	Mon 05/01/15	Thu 19/03/15																		

Project: WRS Move ver 2
Date: Thu 05/02/15

Task Progress Summary External Tasks Deadline
Split Milestone Project Summary External Milestone

ID	Task Name	Duration	Start	Finish	Predecessors	Resource Names	Calendar																																																																																										
							01 Dec '14		08 Dec '14		15 Dec '14		22 Dec '14		29 Dec '14		05 Jan '15		12 Jan '15		19 Jan '15		26 Jan '15		02 Feb '15		09 Feb '15		16 Feb '15																																																																				
							S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S
344	Photo's	10 days	Mon 05/01/15	Fri 16/01/15		WFDC																																																																																											
345	Smart card design	11 days	Mon 12/01/15	Mon 26/01/15		WFDC																																																																																											
346	Gather user information	15 days	Mon 12/01/15	Fri 30/01/15		WFDC / WRS																																																																																											
347	Quote and agree funding	5 days	Mon 26/01/15	Fri 30/01/15		WFDC																																																																																											
348	Produce / Procure smart cards	11 days	Mon 02/02/15	Mon 16/02/15		WFDC																																																																																											
349																																																																																																	
350																																																																																																	
351	Websites	12 days	Fri 27/03/15	Mon 13/04/15																																																																																													
352	Website Migration confirm date	1 day	Fri 27/03/15	Fri 27/03/15		BDC																																																																																											
353	WRS Website handover	1 day	Mon 13/04/15	Mon 13/04/15		WFDC / BDC																																																																																											
354	Web Training confirm	1 day	Tue 31/03/15	Tue 31/03/15		WRS / BDC																																																																																											
355																																																																																																	
356	Helpdesk fully transfer	1 day	Wed 01/07/15	Wed 01/07/15		WFDC																																																																																											
357																																																																																																	
358	Communications Plan	92 days	Mon 23/02/15	Sun 21/06/15																																																																																													
359																																																																																																	
360	Other Moves	64 days	Thu 18/12/14	Tue 17/03/15		WFDC																																																																																											
374																																																																																																	
381																																																																																																	
